

# METROPOLITAN UTILITIES DISTRICT




## GAS INFRASTRUCTURE RELOCATION

M.U.D. must relocate **gas** and **water** mains to eliminate conflicts for the City of Omaha Streetcar Project OPW 54338. For more information on the City's project, please visit <https://OmahaStreetcar.org/>.

**Gas** relocation work will consist of eight phases (see illustration). *This illustration is for informational purposes only and is subject to change.*

Plans for **water** main relocation work are still being finalized.

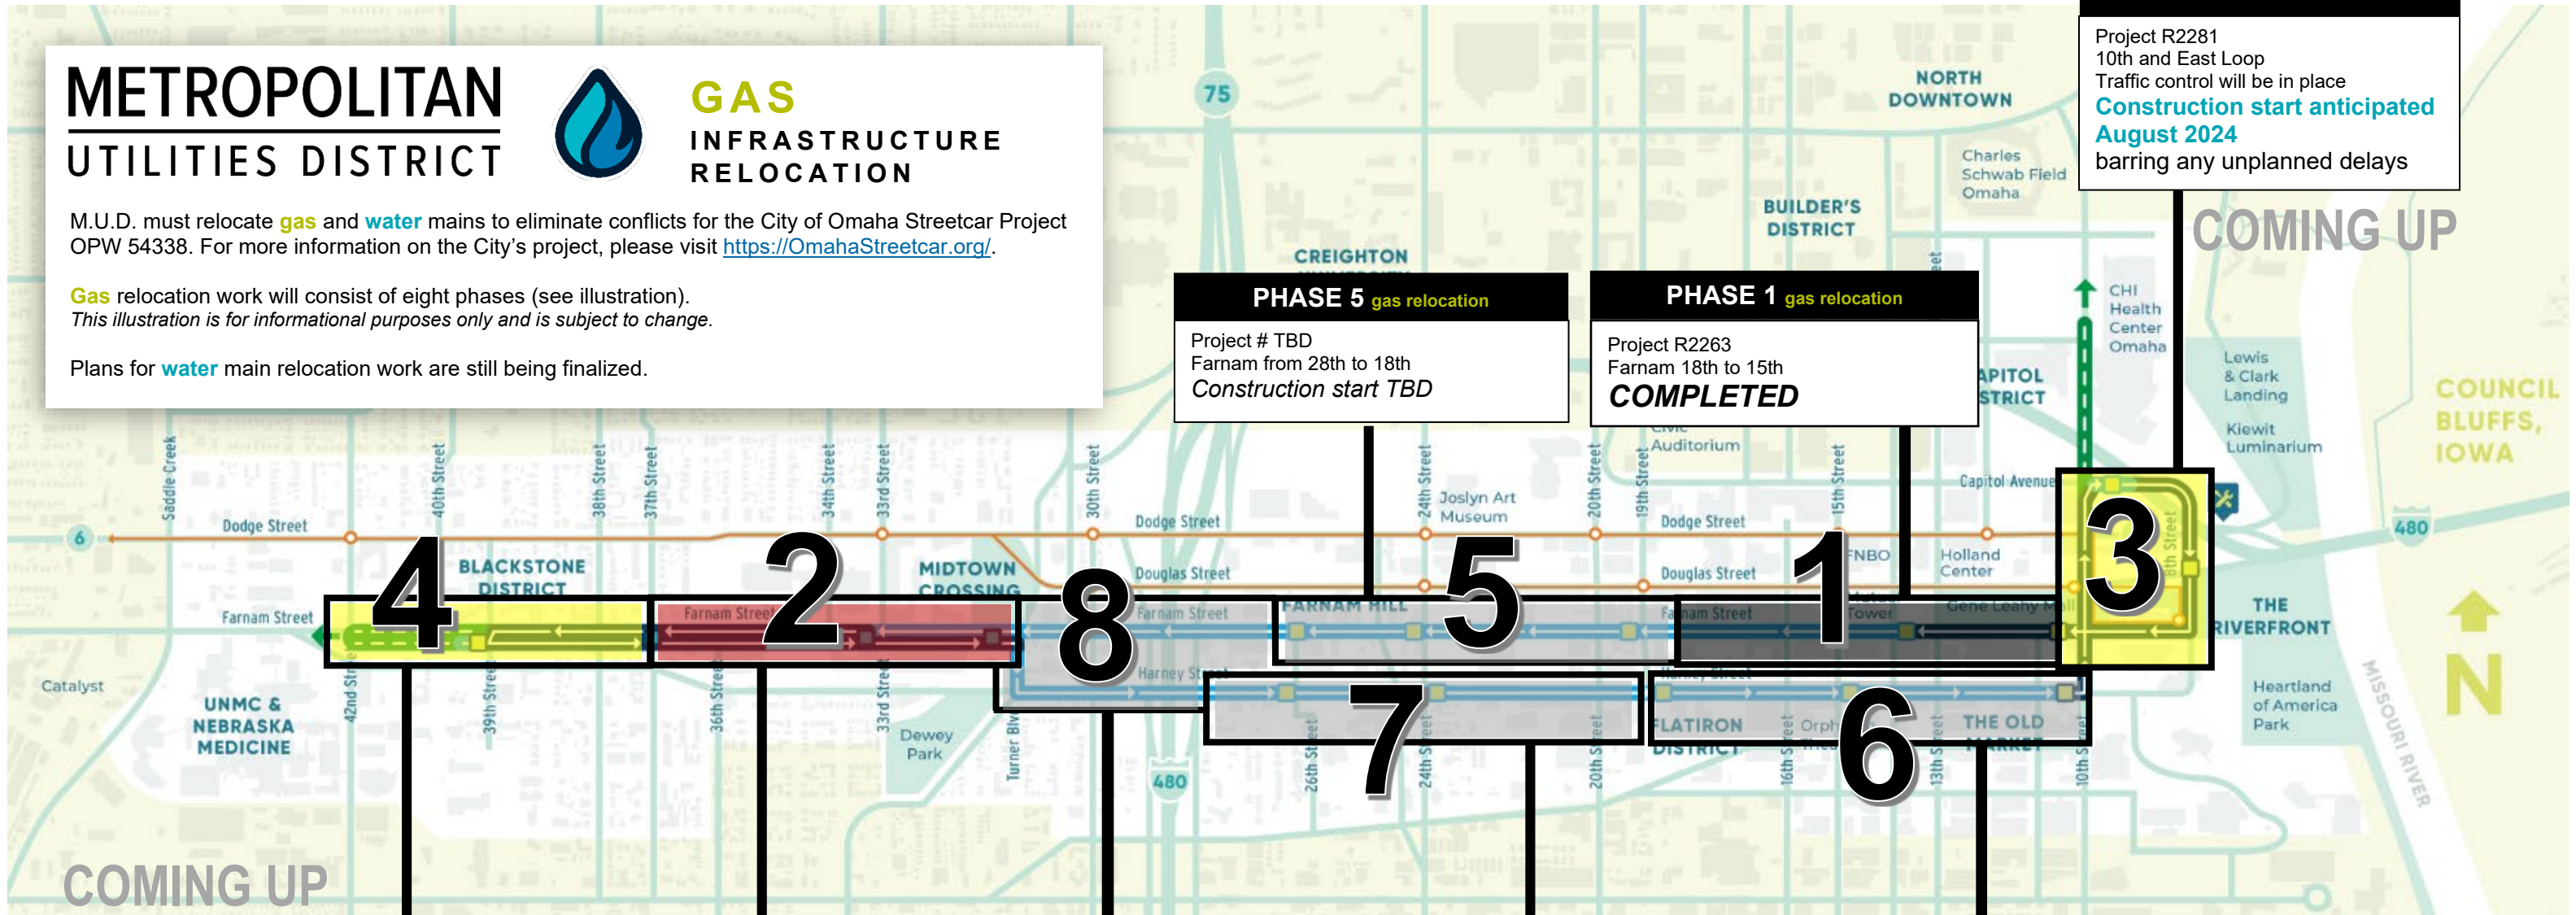

**PHASE 3 gas relocation**  
 Project R2281  
 10th and East Loop  
 Traffic control will be in place  
**Construction start anticipated August 2024**  
 barring any unplanned delays

**PHASE 5 gas relocation**  
 Project # TBD  
 Farnam from 28th to 18th  
**Construction start TBD**

**PHASE 1 gas relocation**  
 Project R2263  
 Farnam 18th to 15th  
**COMPLETED**

**PHASE 4 gas relocation**  
 Project R2289  
 Farnam from 42nd to 37th  
 Anticipate traffic control to be in place the last week of July 2024  
**Construction start anticipated first part of August 2024**  
 barring any unplanned delays

**PHASE 2 gas relocation**  
 R2266  
 Farnam from 37th to Turner Blvd  
**Currently in progress**

**PHASE 8 gas relocation**  
 Project # TBD  
 Farnam and Harney from Turner to 28th  
**Construction start TBD**

**PHASE 7 gas relocation**  
 Project # TBD  
 Harney from 28th to 19th  
**Construction start TBD**

**PHASE 6 gas relocation**  
 Project # TBD  
 Harney from 19th to 10th  
**Construction start TBD**

**IN PROGRESS**  
 started March 22, 2024 **APPROXIMATELY 85% COMPLETE**

- Work is anticipated to be completed the first week of August 2024, barring any unplanned delays.
- Crew started on the west end and is working their way east.
- Traffic control is in place and parking is restricted on the south side of Farnam from 37th to Turner Blvd.
- The entrance/exit to Turner Park (31st Ave) will have a lane restriction. Anticipated start week of July 15.
- Some street and sidewalk repairs have been completed by the city.
- Some excavations remain due to continued necessary work.
- The crew continues to maintain all driveway access during the work.
- Because gas mains are being relocated, services are and will need replaced and/or reconnected in the area. Any inside gas meters may be moved to the outside. A technician from M.U.D. will work with the customers needing gas service work. This reconnection work includes additional holes near the buildings and possibly in Farnam after the new main has been installed.
- All work and dates are approximate and barring any unplanned delays.

**QUESTIONS OR CONCERNS**

Tina Gutschenritter  
 402.504.7770

[CustomerSuccessTeam@mudnebr.com](mailto:CustomerSuccessTeam@mudnebr.com)
